

The City of Oklahoma City May 19, 2015



Oklahoma City Tennis Center

Project No. MP-0449
Oklahoma City Tennis Center Improvements



Project Scope:

Phase 1

- Construct 3 new adult tennis courts
- Construct 6 new youth tennis courts
- Hardscaping to provide access to and from parking and other facilities within the OKC Tennis Center campus

Phase 2


- Construct building to enclose six (6) adult tennis courts
- Hardscaping to provide access to and from parking and other facilities within the OKC Tennis Center campus







Existing Site

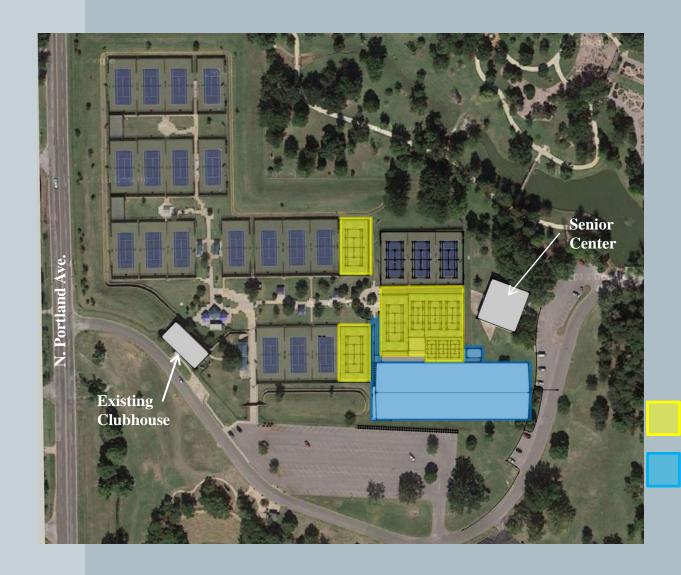

Phase 2







Phase 1: Outdoor Tennis Courts





Phase 2: Indoor Tennis Courts







View from the Southwest









Project Budget and Estimate:

Project Budget

Phase 1 Budget \$520,000
 Phase 2 Budget \$2,775,456
 Total \$3,295,456

Estimates

Phase 1 Construction Estimate: \$519,864
 Phase 2 Construction Estimate: \$2,904,368
 Total \$3,424,232



Project Schedule

February, 2015 Phase 1 Begin Construction

May, 2015 Phase 1 Construction

Complete

May, 2015 Preliminary Report

June, 2015
Phase 2 Final Plans

June, 2015Bid Opening

July, 2015 Award Contract – Begin

Construction


November, 2015 Construction Complete



OKC Tennis Center Improvements





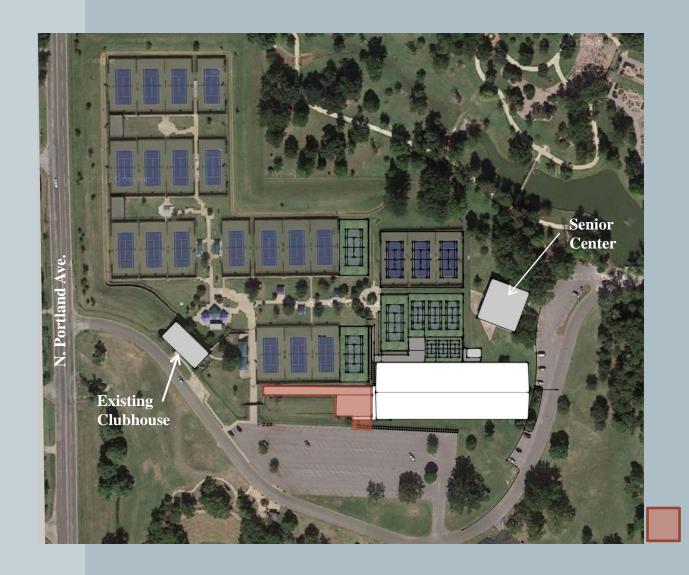

Phase 3: New Clubhouse





The City of Oklahoma City May 19, 2015



Oklahoma City Tennis Center

Project No. MP-0449
Oklahoma City Tennis Center Improvements

